

FLEXIBLE TECHNICAL DELIVERY SCHEDULE & ROADMAP

2-Month Spiral Development Plan, Sprint Cadence, and Reporting Framework

Program: POM Digital Ecosystem

Effective Date: June 2026

Operating Model: Alternating Focus Days, Hybrid Collaboration, and Evidence-Based Reporting

1 Primary Availability Schedule

This schedule is intentionally designed around a **one-day-on / one-day-off delivery rhythm** with controlled stochasticity. Workdays are reserved for focused execution, sprint reviews, architecture decisions, measurable delivery outputs, and scheduled client-facing coordination when required. Off-days are preserved for recovery, academic or personal commitments, and limited communication windows only. **Friday is excluded from the active work schedule.**

Stochasticity principle: delivery planning assumes normal week-to-week variability in blockers, approvals, sick days, emergency issues, infrastructure incidents, and client urgency. The schedule therefore uses fixed anchor days plus explicit buffers, replacement rules, and probability-based risk controls instead of pretending that every week will execute identically.

Table 1: Weekly Availability, Work Cadence, and Delivery Expectations

Day	Availability	Cadence Status		Delivery Intent
Sunday	17:00 – 22:00 Remote	Active	Work-day	Sprint setup, backlog review, architecture notes, dependency checks, and preparation for the main delivery block
Monday	Off / Protected; calls 18:00 – 18:20	Off-Day		No planned delivery; limited phone availability for urgent clarification only
Tuesday	17:00 – 22:00 Remote	Active	Work-day	Backend/API implementation, data modeling, validation tasks, issue closure, and asynchronous review responses
Wednesday	Off / Protected; calls 18:00 – 18:20	Off-Day		No planned delivery; limited phone availability for blockers affecting the next active workday
Thursday	10:00 – 17:00 On-Site/Hybrid	Active	Work-day	Sprint planning, solution review, feature prioritization, client meetings when required, risk decisions, and integration walkthroughs
Friday	Unavailable	No Scheduled	Work	Fully excluded from planned execution, meetings, delivery commitments, phone calls, and reporting obligations
Saturday	Off / Replacement Buffer; calls 13:00 – 13:20	Off-Day	Backup	/ Protected non-delivery day; may replace a missed active day only for sickness, emergency, or approved delivery-critical recovery

1.1 Schedule Rules and Professional Boundaries

- **Core rhythm:** active delivery occurs on Sunday, Tuesday, and Thursday; each active day is followed by a protected off-day.
- **No Friday work:** Friday is excluded from sprint ceremonies, delivery planning, production pushes, routine communication, and phone-call expectations.
- **Replacement-day policy:** Saturday may replace Sunday, Tuesday, or Thursday only when sickness, emergency, infrastructure failure, or unavoidable client escalation prevents normal delivery.

- **Phone-call policy:** off-day calls are limited to one 20-minute window; if a topic requires deeper work, it is moved to the next active workday or the approved replacement day.
- **Flexible execution:** active workdays may shift between remote and hybrid formats when the sprint requires deeper implementation time, in-person alignment, or client-facing coordination.
- **Async discipline:** off-day communication should be limited to concise blockers, approvals, or information that directly affects the next active workday.
- **Delivery accountability:** every active workday must produce a visible artifact: code, diagram, backlog update, meeting note, test evidence, metric note, or decision log.

1.2 Active-Day Operating Blocks

Table 2: Detailed Structure for Each Active Workday

Block	Time Allocation	Expected Output
Planning & Triage	20–30 minutes	Confirm the sprint objective, identify blockers, select the highest-value technical outcome, and update priority order
Deep Implementation	2–4 hours	Execute backend, web, mobile, database, DevOps, or documentation tasks with minimal context switching
Validation Pass	30–60 minutes	Run relevant checks, inspect logs, verify acceptance criteria, and record evidence for weekly reporting
Reporting Note	10–20 minutes	Summarize completed work, unresolved risks, metric changes, and next-action recommendations

Work Rhythm

Sunday → Off Monday → Tuesday → Off Wednesday → Thursday → No Friday → Off Saturday

Availability Philosophy

High-quality delivery is prioritized over daily availability; each active day is designed to be focused, measurable, and decision-ready.

1.3 Client Meeting Windows and Communication Policy

Client meetings, when required, should be scheduled inside active workdays to protect delivery focus and avoid uncontrolled calendar spread. Preferred client-facing windows are:

- **Tuesday 19:00 – 20:00:** remote client discovery, clarification, progress review, or acceptance walk-through.
- **Thursday 13:00 – 15:00:** hybrid or on-site client workshop, integration review, requirements clarification, or milestone demonstration.
- **Sunday 20:00 – 20:30:** short pre-sprint client clarification only when needed to unblock Tuesday implementation.

Off-day client calls follow the same 20-minute limit and must be restricted to urgent blockers. Friday remains unavailable for client meetings, operational calls, and routine follow-ups.

1.4 Stochastic Schedule Controls

The schedule is managed with probabilistic buffers rather than fixed daily assumptions. Each week is classified into one of three operating states:


Table 3: Stochastic Operating States and Response Rules

State	Expected Likelihood	Condition	Response
Green	60–70%	Normal workload, no major blockers, expected approvals available	Execute planned sprint scope and preserve off-days
Amber	20–30%	Delayed approvals, minor illness, client changes, or technical uncertainty	Reduce low-priority scope, use shorter reporting, and reserve Saturday only if needed
Red	5–10%	Critical outage, severe illness, urgent client escalation, or blocked deployment path	Activate replacement-day policy, re-scope sprint commitments, and document recovery actions

2 Document Purpose and Delivery Philosophy


The remainder of this document explains how the schedule translates into a complete technical delivery system. It defines the development method, sprint structure, architecture blocks, milestone gates, reporting statistics, and change-control rules that keep the two-month effort organized without requiring daily work.

The delivery approach follows a **spiral development model**: each cycle moves through discovery, risk analysis, implementation, validation, and review. This keeps the work adaptable while still producing concrete evidence at the end of every active sprint loop.



3 System Delivery Block Diagrams

3.1 Target Ecosystem Architecture

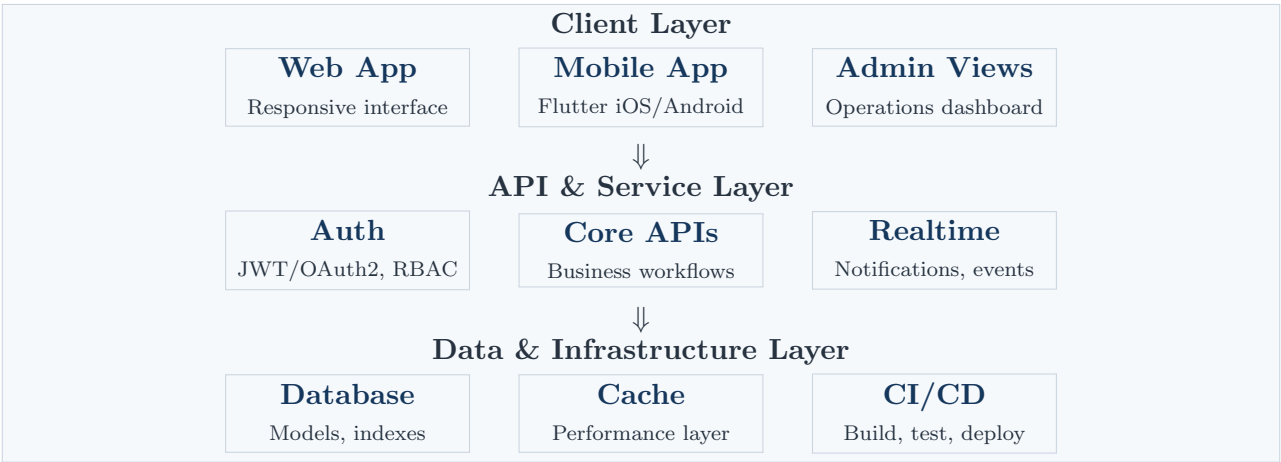

3.2 Sprint Evidence Flow

Sprint Goal ⇒ Risk Check ⇒ Focused Build ⇒ Validation Evidence ⇒ Status Report ⇒ Refined Backlog

Each loop produces an inspectable artifact: code, design note, test result, deployment log, dashboard metric, or documented scope decision.

4 Meeting Notes Framework

Every planned meeting must produce a concise written note. The note is treated as part of the delivery evidence and should be stored with the relevant sprint artifacts.

Table 4: Required Meeting Notes for Recurring and Conditional Meetings

Meeting Type	Preferred Time	Participants	Required Notes
Sprint Setup	Sunday 17:00 – 17:30	Delivery owner and relevant collaborators	Sprint goal, selected backlog items, assumptions, blockers, expected artifacts
Technical Review	Tuesday 21:00 – 21:30	Technical collaborators as needed	Completed work, open defects, validation results, integration risks, next actions
Planning Alignment	Thursday 10:00 – 11:00	Product, operations, and technical stakeholders	Priority decisions, scope changes, risk updates, timeline impact, approvals required
Client Meeting	Tuesday 19:00 – 20:00 or Thursday 13:00 – 15:00	Client representatives when applicable	Client requests, accepted requirements, unresolved questions, commitments, follow-up owner
Emergency Call	Off-day 20-minute window only	Required decision-maker only	Trigger reason, decision taken, time spent, whether Saturday replacement is activated

Meeting-note template: date; meeting type; attendees; agenda; decisions; action items; owner; deadline; risks raised; mitigation selected; follow-up required; impact on sprint scope.

5 2-Month Spiral Engineering Roadmap

The eight-week roadmap is organized into four two-week spirals. Each spiral contains planning, risk review, focused implementation, validation, and reporting. Because availability follows an alternating cadence, each sprint emphasizes fewer but more intentional execution blocks.

5.1 Spiral I: Architecture, Data Model & Delivery Foundation (Weeks 1 – 2)

- **Sprint 1A – Architecture Baseline:** define system boundaries, platform responsibilities, integration flows, repository structure, environment strategy, and backlog taxonomy.
- **Sprint 1B – Data and Security Foundation:** establish database assumptions, authentication model, authorization roles, API conventions, secrets handling, and CI/CD quality gates.
- **Exit criteria:** architecture diagram, prioritized backlog, staging-ready repository structure, baseline API contract, and documented technical risks.

5.2 Spiral II: Web Platform, APIs & Operational Dashboarding (Weeks 3 – 4)

- **Sprint 2A – Web Experience:** scaffold responsive interface, navigation, reusable UI components, onboarding flows, form states, and accessibility baseline.
- **Sprint 2B – API Integration:** connect UI modules to backend services, implement validation, add error handling, and prepare operational dashboard views.
- **Exit criteria:** staging web build, connected API flows, dashboard prototype, error-state handling, performance baseline, and demo-ready feature increment.

5.3 Spiral III: Cross-Platform Mobile Client & Reusable Product Patterns (Weeks 5 – 6)

- **Sprint 3A – Mobile Architecture:** define Flutter project structure, state management pattern, routing, local storage, design tokens, and reusable form components.
- **Sprint 3B – Mobile Integration:** connect mobile client to API services, implement secure session persistence, prepare notification pathway, and compile alpha builds.
- **Exit criteria:** runnable mobile alpha, documented architecture pattern, connected authentication path, reusable component library, and device-testing checklist.

5.4 Spiral IV: Integration, Hardening, Release Readiness & Documentation (Weeks 7 – 8)

- **Sprint 4A – End-to-End Validation:** test core user journeys across web, mobile, backend, data, and deployment workflows; optimize latency and reliability bottlenecks.
- **Sprint 4B – Release Readiness:** finalize deployment runbooks, environment configuration, monitoring dashboards, rollback procedures, architecture handover, and production checklist.
- **Exit criteria:** end-to-end test evidence, release candidate build, monitoring baseline, risk closure report, deployment checklist, and complete technical handover package.

6 Deliverables, Milestones & Acceptance Gates

Table 5: Milestones, Evidence, and Acceptance Criteria

Gate	Timing	Deliverable Evidence	Acceptance Criteria
G1	End Week 2	Architecture pack, backlog, API contract, data model, risk register	Architecture reviewed; core risks ranked; staging foundation operational
G2	End Week 4	Web staging build, integrated API flows, dashboard prototype, test notes	Priority flows usable; API failures handled; baseline metrics captured
G3	End Week 6	Mobile alpha build, reusable components, auth flow, device checklist	Alpha runs on target devices; session handling verified; core flows connected
G4	End Week 8	Release candidate, monitoring baseline, runbooks, handover documentation	End-to-end validation passed; deployment path documented; rollback plan ready

7 Reporting Statistics & Performance Indicators

Progress reporting uses concise quantitative and qualitative indicators. Metrics are reviewed weekly and summarized at every spiral gate to support evidence-based planning while respecting the alternating work schedule.

3

Active Days / Week

Sunday, Tuesday, and Thursday only

85%+

Sprint Completion Target

Committed items completed or formally re-scoped

95%+

Build Reliability

Successful CI checks on protected branches

Table 6: Weekly Reporting Metrics and Interpretation		
Metric Category	Tracked Indicators	Reporting Purpose
Delivery Velocity	Planned vs. completed tasks; spillover ratio; blocked items	Measures execution predictability and identifies planning adjustments
Quality	Defect count; re-opened issues; review findings; test pass rate	Confirms whether increments are stable enough for integration
Performance	API latency; page-load baseline; build duration; database query timing	Establishes technical baselines before scaling usage
Risk	Critical open risks; dependency exposure; unresolved decisions	Shows whether the roadmap is becoming safer and clearer each spiral
Documentation	Decision logs; API notes; runbook updates; architecture revisions	Ensures knowledge transfer and operational continuity

8 Risk Register and Mitigation Plan

Table 7: Primary Risks, Stochastic Triggers, and Mitigations			
Risk	Level	Stochastic Trigger	Mitigation
Sick day or personal emergency	Medium	Active workday becomes unavailable unexpectedly	Activate Saturday replacement only if sprint-critical; otherwise re-scope and document impact
Client urgency outside schedule	Medium	Client requests immediate clarification on an off-day	Use the 20-minute call window; defer implementation to the next active day
Scope volatility	High	Requirements change after sprint commitment	Move new scope into backlog, assess impact, replace lower-priority tasks only by explicit decision
Infrastructure cost overrun	High	Server rent, AI compute, paid APIs, storage, or deployment resources exceed assumptions	Treat costs as external expenses; obtain provisioned budget before use
Technical blocker	Medium	API, database, build, authentication, or deployment path blocks progress	Log blocker, isolate minimal reproducible issue, use next active day for focused resolution
Approval delay	Medium	Required decision is not available before implementation window	Continue with non-blocked tasks; record assumption and request decision in next meeting note

External Cost and Resource Provisioning

The delivery agreement covers planning, development execution, validation, documentation, and reporting within the stated schedule. **External operational expenses are not included in the agreement.** This includes server rentals, cloud hosting, managed databases, storage, paid APIs, domain services, deployment tools, AI compute, model inference, GPU usage, vector databases, monitoring subscriptions, and third-party SaaS tools.

Any required external infrastructure or AI-compute budget must be provided separately by the CEO or the designated budget owner before activation, upgrade, or scale-up. No paid external resource should be assumed as included unless explicitly approved and provisioned in writing.

Future Client and Subsidiary Project Commercial Policy

This policy applies only to future client projects, subsidiary projects, external engagements, or commercial work introduced through or around the POM ecosystem. **It does not apply to the core POM development work described in this roadmap.**

- **Initial down payment:** any future client or subsidiary project requires a non-refundable **20,000 EGP** down payment before discovery, planning, review, or implementation begins.
- **Delivery success fee:** upon final delivery, acceptance, or handover, an additional **20% of the total project cost** is due.
- **Minimum viable engagement:** a single client project below **20,000 EGP** will not be accepted alone.
- **Batching rule:** smaller projects may be grouped into a batch of two or more projects, provided the combined batch value is at least **30,000 EGP** before work begins.
- **Batch interpretation:** a batch is treated as one commercial engagement for scheduling, delivery planning, payment eligibility, and prioritization.
- **Start condition:** no future client or subsidiary work begins until down payment, scope, acceptance conditions, and payment responsibility are confirmed in writing.

Plain interpretation: future external projects require financial commitment before work starts. Small projects are only considered when grouped into a commercially meaningful batch of at least 30,000 EGP.

Governance, Risk Control & Change Management

- **Backlog control:** all new scope enters the backlog, receives priority, and is assigned to a suitable sprint or deferred with rationale.
- **Risk control:** each spiral maintains a ranked risk register covering architecture, security, dependencies, schedule, infrastructure, and product uncertainty.
- **Change control:** scope adjustments are accepted when they preserve release readiness, reduce risk, or improve measurable user value.
- **Definition of done:** work is complete only when implementation, validation evidence, documentation, and reporting notes are updated.

Digitally acknowledged and signed by

Sherif Rashwan

Sherif Rashwan
Signature Date: June 2026
